



Get the latest updates on the renovation of Mayville State's historic Old Main! Follow progress, upcoming projects, and more as PCL/Community Contractors work to preserve its legacy and shape its future.

PROGRESS UPDATES


- **Basement:** Painting is nearing completion. Flooring preparations are underway, and MEP device installation continues.
- **First floor:** Door frames and slabs are being installed. MEP overhead devices and lighting installation are progressing, and veneer paneling is wrapping up.
- **Second floor:** Flooring installation is ongoing, along with MEP device installation, finish work, and final cleaning.
- **Third floor:** Crews are addressing pre-punch list items and completing cleaning activities.
- **Fourth floor:** Final punch list work is underway.



Final punch list work is underway on the fourth floor.



Lobby preparation is nearly complete and ready for paint.

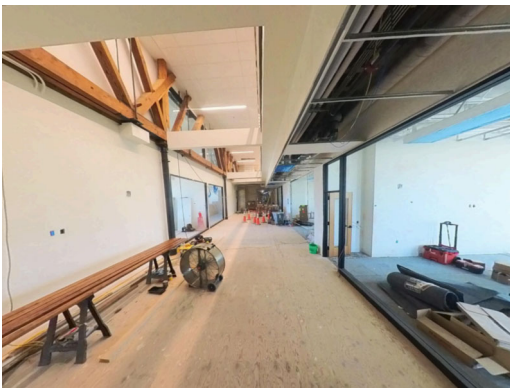

Flooring installation continues on the second floor as lighting and device installation are finalized.

UPCOMING WORK

In the coming weeks, crews will focus on:

- Installing door frames and door slabs
- Completing flooring installation
- Beginning theater millwork installation
- Installing metal handrails
- Installing glazing and glass systems

DID YOU KNOW?

One of the key quality-control tools used on the project is BIM Issue Tracking. This process allows the team to identify, document, and assign issues directly within the project's digital drawings. By providing clear ownership and visibility, BIM Issue Tracking helps teams resolve concerns efficiently and maintain high-quality standards throughout construction.

SAFETY TOPIC

With summer temperatures in full swing, staying hydrated remains a top priority. Anyone working outdoors or in high-temperature environments should drink water frequently and monitor themselves and their coworkers for signs of dehydration or heat-related illness. Taking proactive steps can help prevent serious health and safety risks.

